PAVING THE WAY: EXPLORE THE NEW

CBR TRAIL

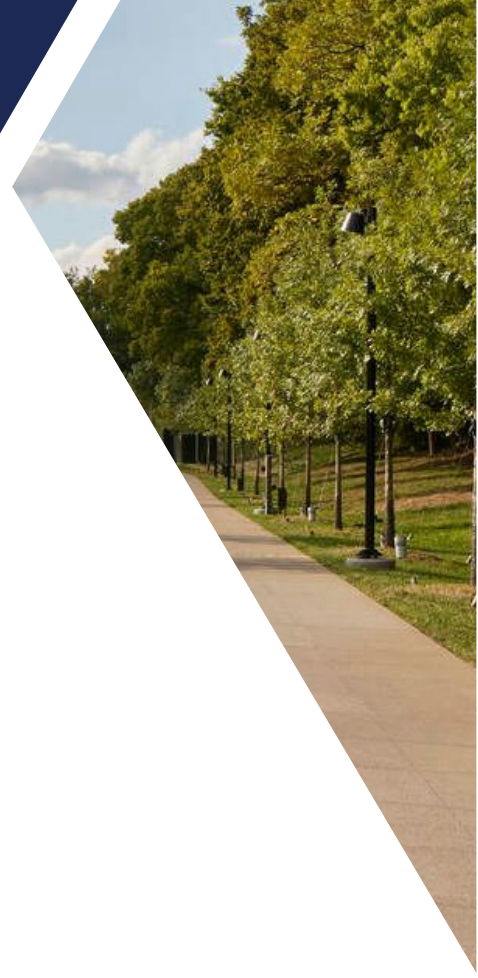

CBR Trail construction is ongoing in the Town of Addison. The following is an update of construction work performed during the month of June 2026.



TOWN OF **ADDISON**

COTTON BELT REGIONAL TRAIL *(CBR TRAIL)*

CONSTRUCTION STATUS NEWSLETTER

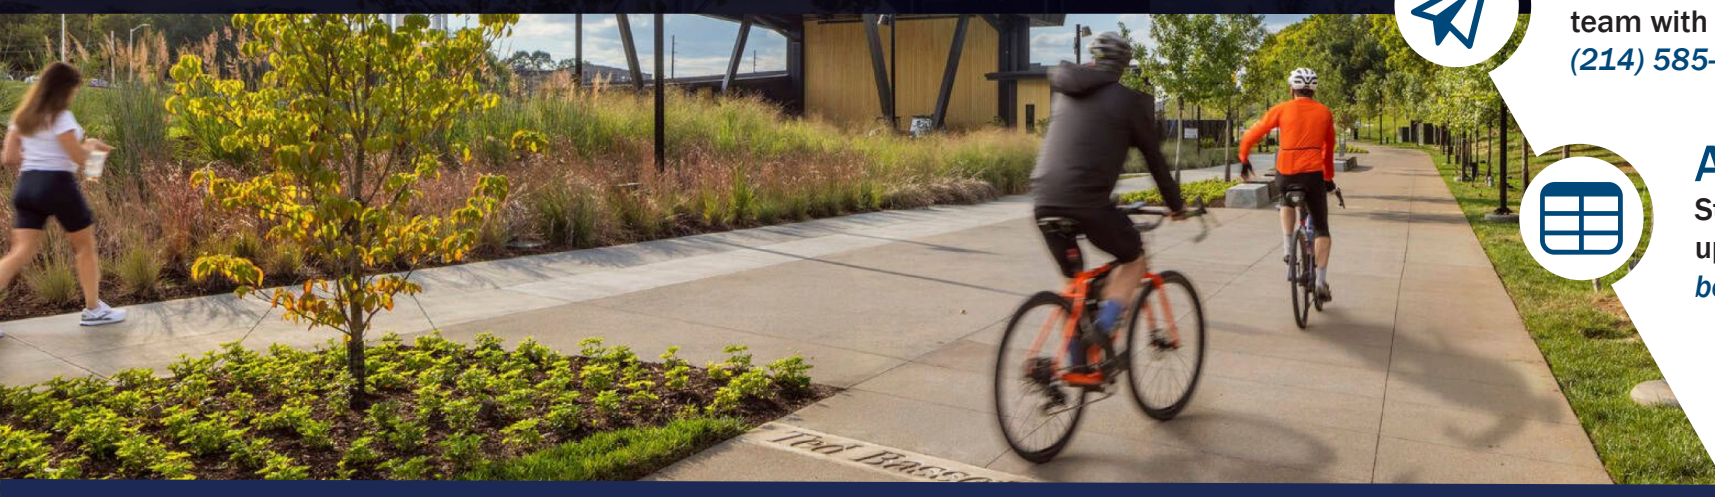

PROGRESS PHOTOS

See photos of the trail constuction:
https://tinyurl.com/CBRT-Addison-Jun2026

MONTHLY UPDATES

Stay tuned for upcoming monthly newsletters!

CONTACT US!

Reach out to the project team with questions at:
(214) 585-7308

ACTIVITY

Stay posted with updates by roadway *below!*

CONSTRUCTION UPDATE MAP

LEGEND

- TRAIL IN PROGRESS
- TRAIL COMPLETE
- PHASE 3A: MARSH LN. TO MIDWAY BRIDGE

ADDISON (1.1 MILES)

WORK DATES: 05/14/25 - 11/09/26
TOTAL FEET (TF): 5,808 TF
TF INSTALLED: ~3,046 TF
TF REMAINING: ~2,762 TF
BRIDGE PROGRESS: 58% COMPLETED
TRAIL PROGRESS: 60% COMPLETED



BRIDGE 22P:
MIDWAY ROAD
WORK DATES:
05/15/25 - 11/09/26

UPDATES BY ROADWAY

LOCATION	CONSTRUCTION ACTIVITY	START	FINISH*	% COMPLETE
Surveyor Blvd. to Midway Bridge	Drainage scope is on hold until the FIFA World Cup has ended, trail construction to follow.	Dec. 19, 2025	Nov. 23, 2026	50%
Midway Bridge	Spans 1-4 steel have been set. Superstructure scope is about 25% complete.	Nov. 3, 2025	Apr. 20, 2027	59%
Midway Bridge to Railroad Crossing at 2354	Work is scheduled to begin on July 20th.	Jul. 20, 2026	Dec. 14, 2026	0%
Railroad Crossing at 2354 to Addison Rd.	Panels for future crossings have been installed. No work will occur until the Midway Bridge progresses.	Jan. 26, 2026	Aug. 31, 2026	10%
Addison Rd. Intersection (Incl. RR Crossing)	Signage and striping are complete. Minor fence restoration remains	Jul. 21, 2025	Jul. 31, 2026	99%
Addison Rd. to Quorum Dr.	Trail and handrail are complete.	Jun. 9, 2025	Feb. 6, 2026	100%
Quorum Dr. Intersection	Trail, signage, striping and final clean-up is complete	Sep. 29, 2025	Jun. 30, 2026	100%
Quorum Dr. to Spectrum Dr.	Signage, striping, delineators, bollards and final clean-up is complete.	Nov. 3, 2025	Jul. 1, 2026	100%
Spectrum Dr. Intersection	Signage, striping and final clean-up is complete	Jan. 5, 2026	Jul. 1, 2026	100%
Spectrum Dr. to DNT SB	Trail and handrail are complete.	Jun. 23, 2025	Feb. 27, 2026	100%

**Finish dates correspond to construction end dates, not dates which the trail will be open to the public.*
